

2019 Bituminous Street Improvements St. Joseph, Minnesota



STJOE 147693

Project Update

Project Contacts

General Contractor

Knife River Corp.

Project Manager

Andy Hicks

andy.hicks@kniferiver.com

763-286-0678

Project Superintendent

Todd Puhalla

320.248-1508

Subcontractors

Sewer & Water Main

C&L Excavating

Kevin Cox

320.363.1221

Traffic Control

All State

Manny Kissner

320.685.9911

Concrete Flatwork

West Star Curb

Dean

320.764.9582

Turf Establishment

North Star Landscaping

Sean Grefe

320.597.2500

Grading

Craig Bardson Excavating

Ben Bardson

320.845.4952

City Engineer

Randy Sabart, PE

320.229.4348

rsabart@sehinc.com

SEH Construction Observer

Jerry Siegfried

320.980.4107

jsiegfried@sehinc.com

May 2020 | Project Update No. 3

Hello and welcome again to the *2019 Bituminous Street Improvements Project Update*. The project team would like to thank you for your cooperation on the project last year. Your continued patience and understanding makes difficult construction move ahead much more smoothly. For those of you who have contacted SEH with questions about the project, we will continue to make every attempt to provide answers to you in a timely manner. We encourage you to call or email with questions.

For any questions, Jerry Siegfried, SEH's Project Representative, will be on-site during construction to observe project progress and the Contractor's work. Jerry is the fastest link to problem solving because he communicates directly with everyone on the construction team. Do not hesitate to contact Jerry with any questions you may have. If you are unable to reach Jerry in the field, please contact Bill Zidon at the SEH Office at 320.229.4309.

Schedule Update

The first layer of bituminous has been completed on Old Highway 52, Cypress Drive, Elm Street, Baker Street, Callaway Street, 12th Avenue SE, Pondview Lane E, and 13th Avenue SE and all concrete flatwork has been completed on the project. Paving, aggregate shouldering, and striping have been completed on Jade Road.

The Contractor will complete the remaining work early this construction season. This work consists of the following:

- Edge milling and resurfacing portions of 4th Avenue SE, Western Court, 12th Avenue SE, Pond View Lane, Callaway Street, Cary Court, Cedar Court, Dale Street, Birch Street W, Ash Street W, and 1st Avenue NW will begin May 5th.
- Milling and paving 4th Avenue NE will commence May 5th and will be completed by May 8th, weather permitting.
- The final layer of bituminous will be paved between May 11th – 13th on Old Highway 52, Cypress Drive, Elm Street, Baker Street, Callaway Street, 12th Avenue SE, Pondview Lane E, and 13th Avenue SE.
- Finalizing turf establishment on all disturbed areas will begin on Jade Road May 4th and final clean-up will continue throughout the remainder of the project areas.

The final completion date for the project is July 10, 2020.


Description of Remaining Work

The street resurfacing portion of the project consists of edge milling the outside 6 feet of the existing pavement about 1-inch deep and constructing a new 1.5-inch thick layer of bituminous pavement on 1st Avenue NW, W Birch Street, W Ash Street, 4th Avenue SE, Western Court, 12th Avenue SE, Callaway Street, Pondview Lane, Cary Court, Cedar Court, and Dale Street. There will also be some spot pavement reconstruction areas.

4th Avenue NE will be resurfaced by removing (milling) the full thickness of the existing pavement surface and paving two new layers of bituminous pavement on the existing aggregate base.

Construction Site Safety

There will be some deep utility trench construction and, of course, heavy machinery operating on the construction site. Heavy equipment and construction in progress can be strong attractions to everyone, especially children. Warn your children not to play near machinery and construction material storage areas. Your help in keeping children and other bystanders away from the construction area will ensure that the project will progress smoothly!

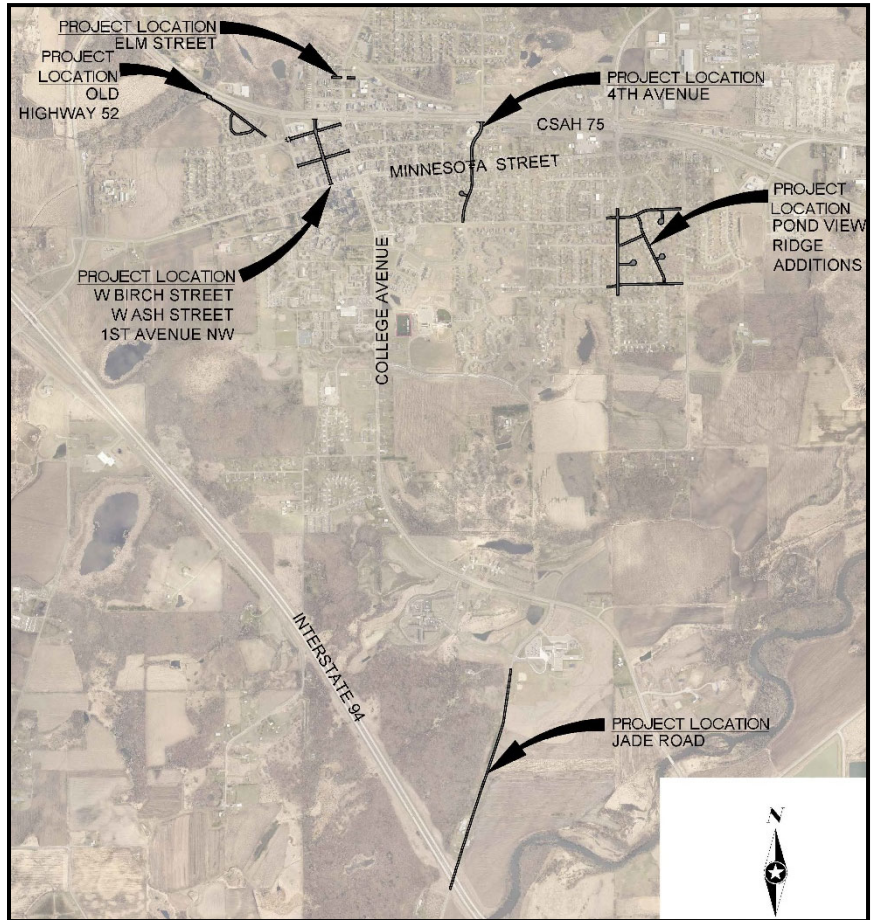

Short Elliott Hendrickson Inc.
1200 25th Avenue South
P.O. Box 1717
St. Cloud, MN 56302-1717



Project Update

2019 Bituminous Street Improvements
St. Joseph, Minnesota
